

Mission Success Starts With Safety



SSC Construction Contractor Safety Meeting

April 7, 2022



Mission Success Starts With Safety



Contact Info:

NASA Safety

Matthew Scott

matthew.r.scott@nasa.gov

228-688-1537

Construction Safety

Donna Dubuisson

donna.a.dubuisson@nasa.gov

228-688-1167

Construction Safety

Elizabeth Calantoni

elizabeth.calantoni@nasa.gov

228-688-1804

B2 Test Stand


Neil Toupin

neil.s.toupin@nasa.gov

228-688-1109

A1 Test Stand

<http://constructionsafety.ssc.nasa.gov/>



Mission Success Starts With Safety



Contact Info:

NASA Safety

Mike Rewis

mike.j.rewis@nasa.gov

228-688-2663

Construction Safety

Frank Olinger

milford.f.olinger@nasa.gov

228-688-1766

Construction Safety

Amanda Ball

amanda.s.ball@nasa.gov

228-688-1422

Construction Safety

Ronnie Good

ronald.w.good@nasa.gov

228-688-1487

Construction Safety

<http://constructionsafety.ssc.nasa.gov/>



Mission Success Starts With Safety



Contact Info:

BASTION/SACOM Safety

Donald Smith, CHST

donald.g.smith-1@nasa.gov

228-688-1085 phone

228-234-0639 Cell

Mark Bridenbeck, TES

mark.a.bridenbeck@nasa.gov

228-688-1732 phone

228-313-0188 Cell

John Lindsay, CSP

john.d.lindsay@nasa.gov

228-688-2557 phone

288-688-3503 fax


Will Davis

william.b.davis@nasa.gov

228-688-3193 phone

228-688-3503 fax

<http://constructionsafety.ssc.nasa.gov/>




Mission Success Starts With Safety



Construction Safety

SSC Construction Inspection
Safety Findings/Stats

March 2022



Construction Safety Report: 01 March – 31 March 2022

Findings: 0


Level 1 Severity : 0

(Corrected on the spot)

Level 2 Severity : 0


(Corrective action documented)

Mishaps: 0 / Close Calls: 0



Discussion Topics

- SSC Safe at Work Protocol Updates
 - <https://sscsos.com/>
- 2022 Construction Safety Stand Down
- Safety Observations
- Safety Topic
- Other




Safety Observations

- SCWI -8715-0008, Section 7: Safety and Health Plans

7.1 Contractor's Safety and Health Plan

1. The contractor shall submit a current, comprehensive, written project-specific Safety and Health Plan that interfaces with the contractor's overall Safety and Health Program. The Contractor shall address each of the elements/sub-elements in the outline contained in Section 7.2 in the order that they are provided in that Section. If an item is not applicable because of the nature of the work to be performed, the Contractor shall state this exception and provide a justification (e.g. Diving Operations: NA, there are no diving operations anticipated on this job.). The plan shall show compliance with Federal OSHA Safety and Health Standards 29 CFR 1904, 29 CFR 1910, and 29 CFR 1926. In addition the contractor's safety and health plan shall show how the contractor will meet the NASA safety requirements.
2. Understanding that the Safety and Health Plan is submitted prior to work starting and that some project-specific information is not yet known (e.g., subcontractors to be used, type of fall protection to be used at a certain point in time, specific cranes or other load handling equipment to be brought on site, etc.), the known information shall be provided and additional information added at each preparatory phase/meeting along with the appropriate AHAs.
3. A copy of the contractor's project-specific, accepted Safety and Health Plan shall be made available upon request.



Safety Observations

- Sinkhole after recent weather:





Hot Work Safety



SACOM Safety Bulletin and NASA Safety Center (NSC)

On February 24, 2022, at Michoud Assembly Facility (MAF) approximately 10:30 AM, an employee working from an aerial lift was torching crane rails in Building 103. Sparks from the torching operation started a fire in the fire protection blanket which was draped around the aerial lift.

Safe Plan of Action

The fire was suppressed using fire extinguishers and a water bucket by the work crew. Security was notified and dispatched the local fire department to respond to the scene. No injury or property damage occurred from this mishap. Thankfully, the work crew was prepared in case of a fire.

Torching activities are considered hot work, which are permit-required activities. There are many areas to consider when planning hot work activities. Remember that all scheduled hot work needs to include proper fire protection, Personal Protective Equipment (PPE) and a fire watch. Prior to any hot work being performed, you must ensure that all fire hazards, including combustible materials, are removed or protected with guarding to confine any heat and sparks. Fire extinguishing equipment, including the proper portable fire extinguisher and buckets of water or sand, must be immediately accessible in case a fire is produced. Knowing what is required in the hot work permit and being properly trained are imperative for hot work activities to be completed safely.

Hot Work Safety

SACOM
SAFETY BULLETIN

At MAF on 02/24/2022, at approximately 10:30 AM, an SS Contractor working from an aerial lift was torching cover rails in B103. Sparks from the torching operation started a fire in the fire protection blanket draped around the aerial lift. No injuries occurred from the mishap.




Tips to avoid mishaps like this:

- Use fire rated thermal blankets or curtains to cover combustibles that must remain inside the 35-ft. radius of the hot work area
- Always have a verified fire extinguisher present, and ensure the staff is trained to properly use it
- Perform regular housekeeping inspections to ensure area is clean of combustibles and flammable material/chemicals
- Maintain a fire watch after welding or cutting operations to detect and extinguish possible smoldering fires.

Remember, hazard identification and mitigation are keys to your safety!

**SSC's Hot Work
Program
Procedure
Requirements are
outlined in Work
Instruction
[SCWI-8838-0002](#)**

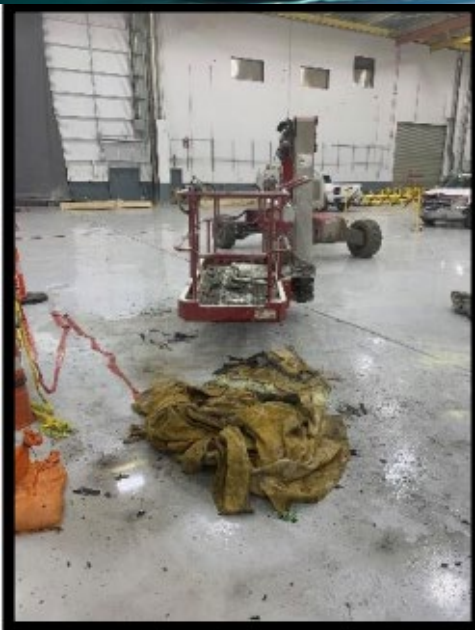


Photos of the mishap were included in the SACOM Safety Bulletin which was sent to all employees. The bulletin included information for avoiding future hot work mishaps.

HOT WORK PERMIT/FIRE HAZARD INCIDENTS AT NASA

Most mishaps can be avoided when operators follow the proper protocol of obtaining a hot work permit and removing potential fire hazards before starting work. Here are examples of incidents that have occurred:

- ❖ A Class A fire caused building damage when paper and trash ignited outdoors. No hot work permit was obtained and there were no fire extinguishers available at the work location.
- ❖ An employee was welding without a hot work permit, unknowingly near an area with stored explosives. A fatal explosion could have occurred if a hot spark had contacted the explosives.
- ❖ An auditor identified poor housekeeping, including loose papers, trash and debris, in a storage area for explosives, which presented a fire hazard.





Questions



<http://constructionsafety.ssc.nasa.gov/>
