# SSC Construction Inspection Safety findings

June, 2009

Prepared/presented by:
Daryl Kosturock, Safety Inspector
Bastion Technologies

## Contact Info:

Buddy Newbold buddy.newbold-1@nasa.gov 228-688-3152 phone 288-688-3701 fax

Daryl Kosturock
<a href="mailto:daryl.kosturock-1@nasa.gov">daryl.kosturock-1@nasa.gov</a>
228-688-3641 phone
228-688-3701 fax

John Rhodes
<a href="mailto:john.d.rhodes-1@nasa.gov">john.d.rhodes-1@nasa.gov</a>
228-688-2462 phone
228-688-3701 fax

http://constructionsafety.ssc.nasa.gov/

## Construction Safety Findings: 29 May - 04 June 2009

### Findings Total: 1

- Serious Findings: 0
- Less than Serious Findings: 1
  - Electrical: 1
    - Contractor found using two extension cords that were missing their ground pins. 29 CFR 1926. 404

### Mishaps / Close Calls: 1

- Close Call: 1
  - During an excavation operation, the contractor found two previously unidentified buried utilities and a ground-grid wire, all within close proximity of each other. The ground wire was the only item that was damaged.

## Construction Safety Findings: 05-11 June 2009

- Findings Total: 0
  - Serious Findings: 0
  - Less than Serious Findings: 0
- Mishaps / Close Calls: 0

## Construction Safety Findings: 12-18 June 2009

## Findings Total: 0

- Serious Findings: 0
- Less than Serious Findings: 0

### Mishaps / Close Calls: 3

#### Mishaps: 1

While straightening out a spray line, walking backwards, an employee fell off the slab of the test stand (approx. 14 inches). The employee received a sprained left knee. The injury resulted in restricted duty and a pain medication prescription.

#### Close Calls: 2

- Two employees were attempting to make repairs to a mooring pier from a skiff. One of the employees reached too far, lost balance and fell into the canal. The employee was immediately recovered and was not injured.
- Two employees were observed violating a company safety policy by being attached to the wrong fall protection for the area that they were in, making it difficult to rescue them if they fell.

## Construction Safety Findings: 19-25 June 2009

## Findings Total: 1

- Serious Findings: 0
- Less than Serious Findings: 1
  - Trenching: 1
    - Employees failed to hand dig within six feet of a known and properly marked buried utility. SSTD-8070-0119-MISC section 5.2.3

### Mishaps / Close Calls: 1

- Mishaps: 1
  - A contractor damaged a buried two inch natural gas line during and excavation activity. The line did not appear to be properly located.
- Close Calls: 1
  - A contractor damaged a buried electric line during an excavation activity. The line was on the drawings and was properly identified.

## Construction Safety Findings: 26-30 June 2009


- Findings Total: 0
  - Serious Findings: 0
  - Less than Serious Findings: 0
- Mishaps / Close Calls: 0

## Summary


- Total Findings: 2
- Serious Findings: 0
- Less than serious Findings: 2
- Close Calls: 4
- Mishaps: 2
- Injuries: 1

### 2009

Construction Safety Findings by category:

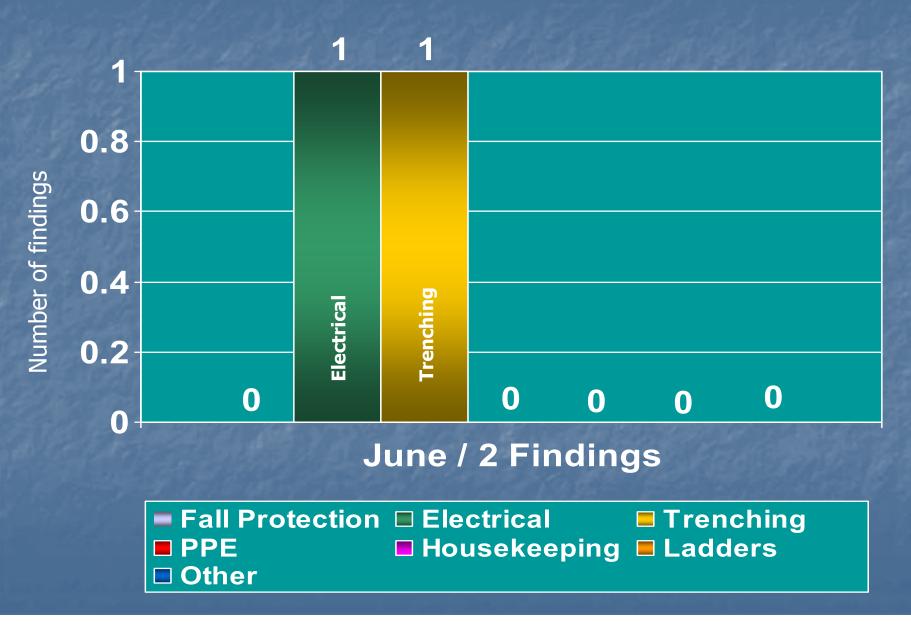

2009 Total Construction Safety Findings by month Total: **22** 6 5 Number of findings 4 3 3 2 2 0 0 0 0 January February March August September June April November July Мау December

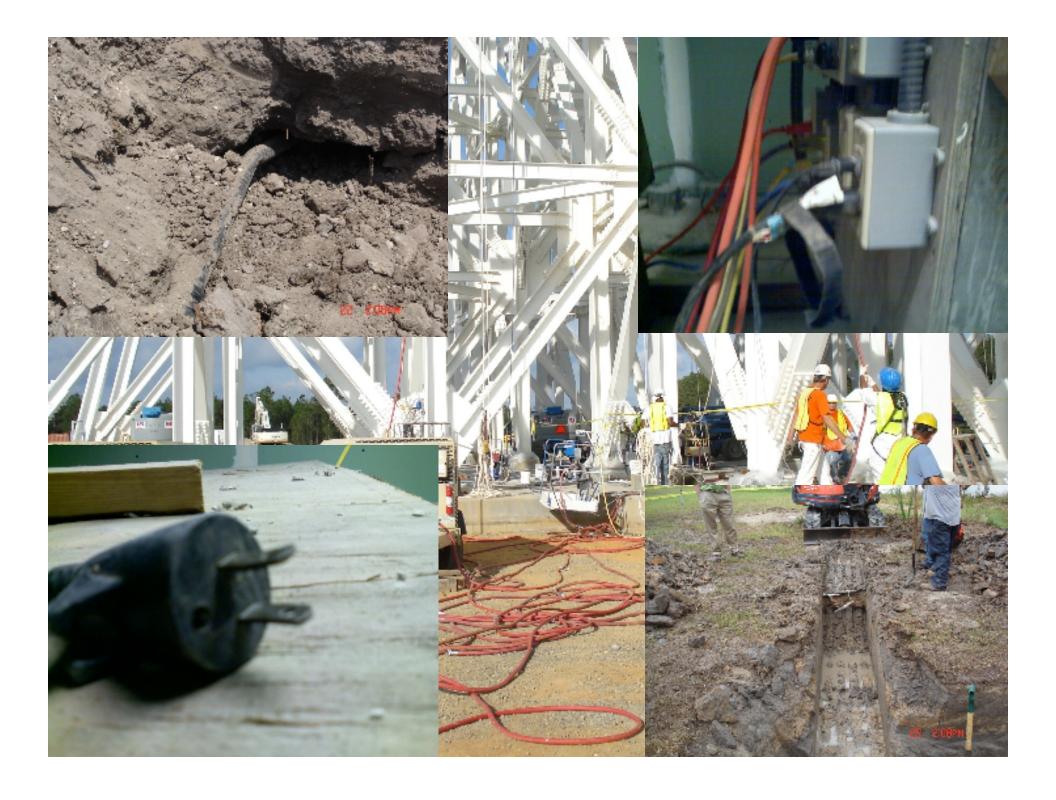

## Health Hazards at work

The following video demonstrates why it is important to be aware of the hidden health hazards that may exist at your work site!





# The only excuse for poor safety is poor planning.

